


RIGGING WEIGHTS - PER CRANE			
COMPONENT	QTY	WEIGHT	TOTAL WEIGHT
Ø1½"x15' WIRE SLING	2	4.16#/FT	124.8
35t SHACKLE	2	45#/EA	90.0
10'-10" TO 18' EXP. SPREADER BAR	1	906#/EA	906.0
25t SHACKLE	4	27.78#/EA	111.1
Ø1½"x25' WIRE SLING (DROPS)	2	4.16#/FT	124.8
W14x233 HEADER BEAM	1	233#/FT	5825
LIFTING LINK	2	278#/EA	556
BRIDGE CLAMPS	8	40#/EA	320
TOTAL			8058

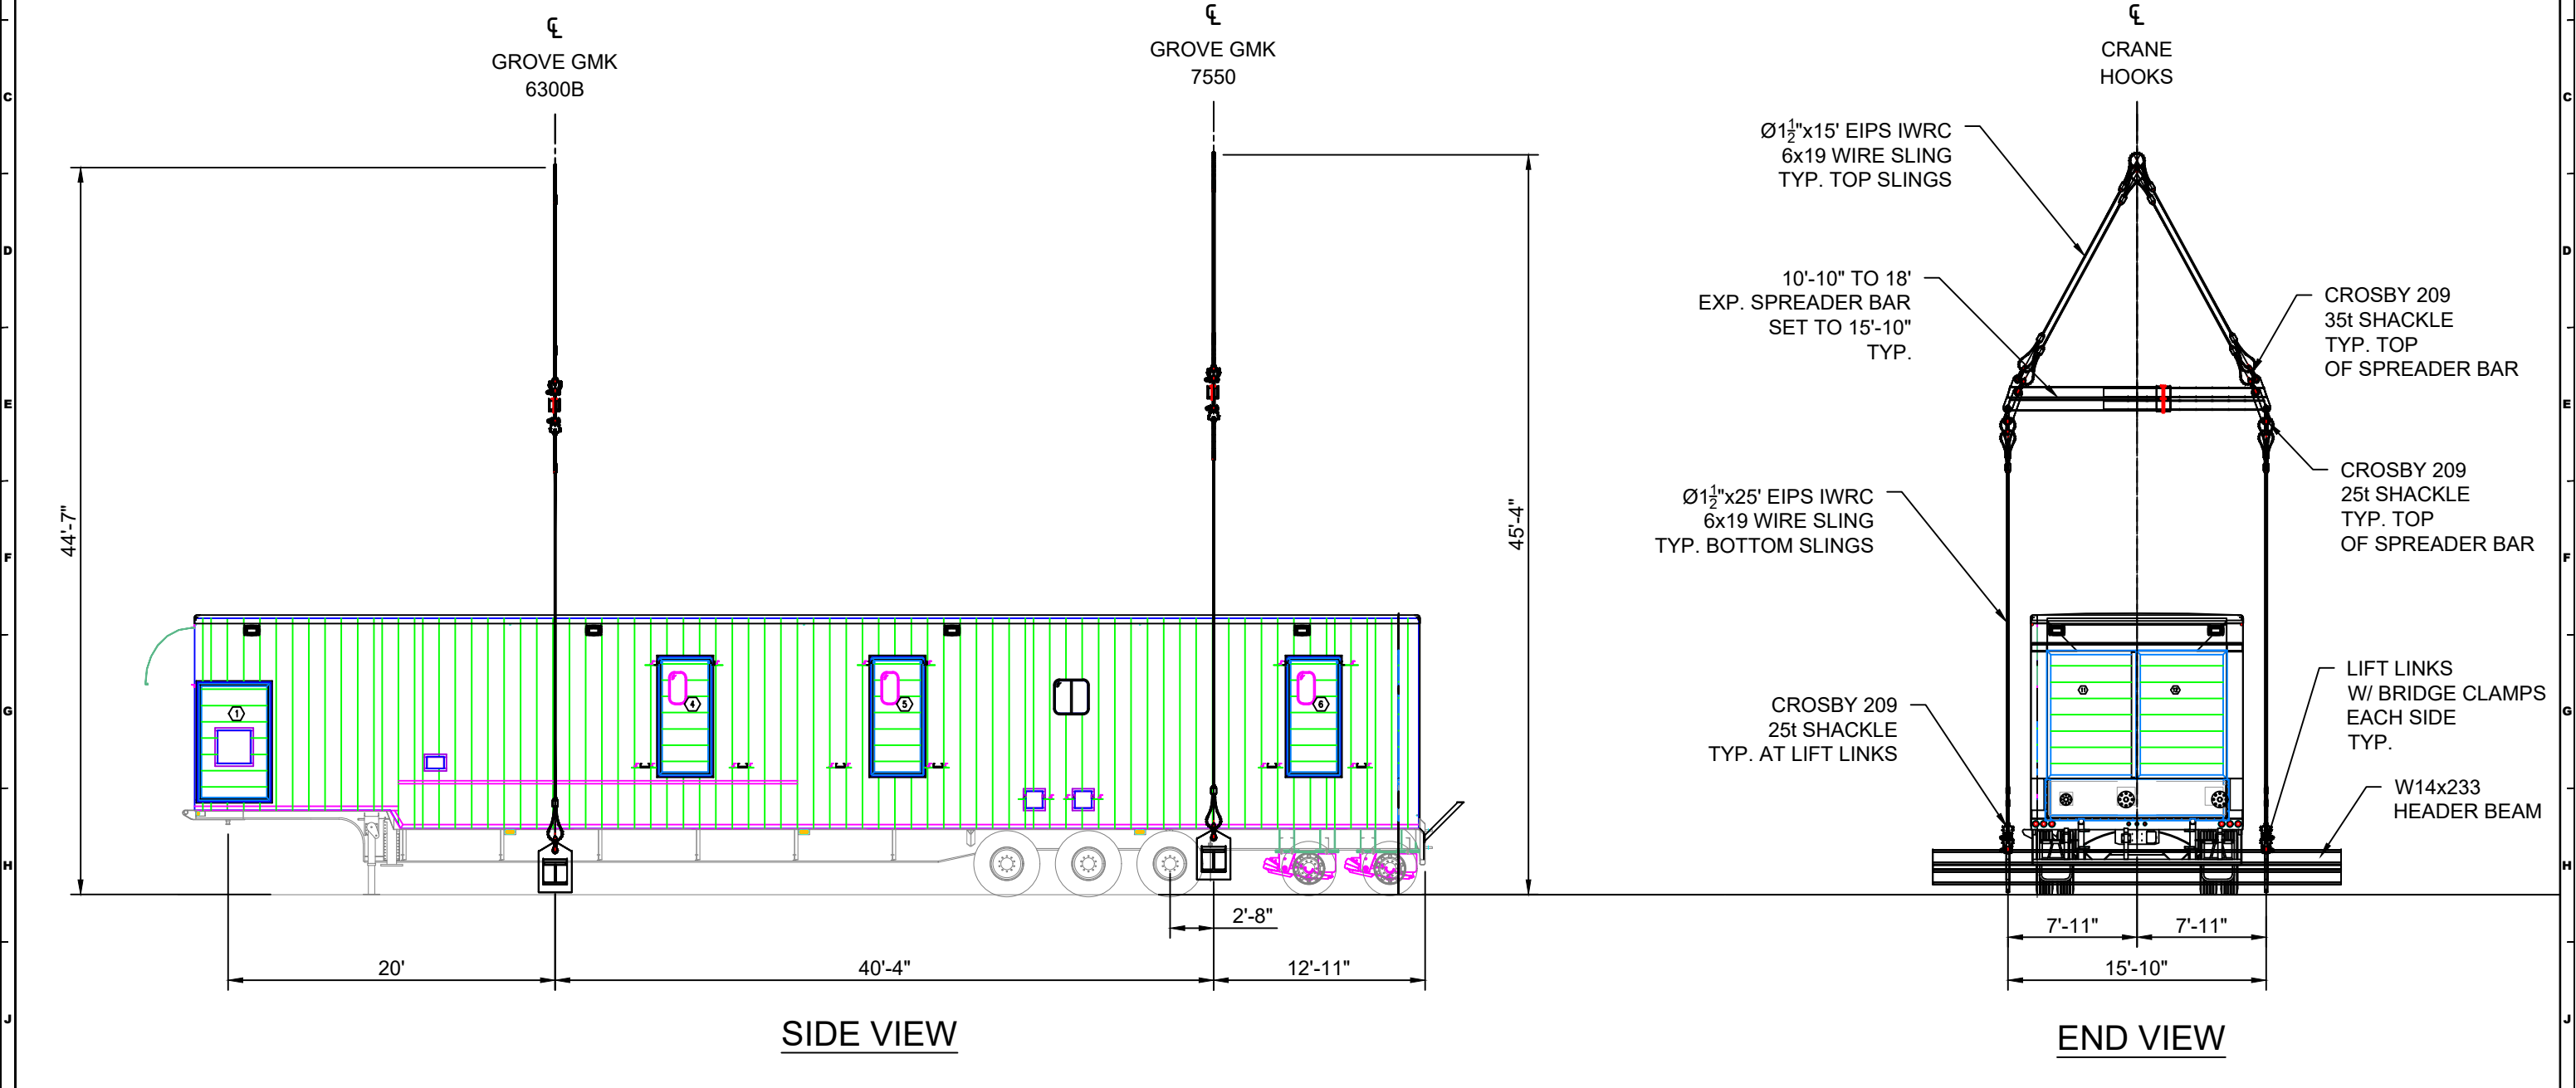

GENERAL NOTES:
 1. LOAD CENTER UNKNOWN.
 2. BEAM LOCATIONS MAY VARY. LOAD SHALL BE LIFTING OFF THE GROUND A COUPLE INCHES AND THE LEVELNESS SHALL BE CHECKED.

REV #	REVISIONS	DATE	REV BY	CHK BY

NESS CAMPBELL
CRANE + RIGGING

OFFICES:
 SEATTLE DIVISION - 1821 180TH ST S.E. BOTHELL, WA 98031 (206) 784-1054
 PORTLAND DIVISION - 5730 NE 138TH AVE PORTLAND, OR 97320 (503) 283-3111

DISCLOSURE:
 THIS DOCUMENT IS THE PROPERTY OF NESS & CAMPBELL CRANE, INC. THIS DOCUMENT SHALL NOT BE REPRODUCED, COPIED, DISCLOSED TO OTHERS, OR USED FOR ANY PURPOSE OTHER THAN THAT FOR WHICH IT WAS FURNISHED WITHOUT PRIOR WRITTEN CONSENT OF NESS & CAMPBELL CRANE, INC.

TITLE:	TRAILER HOISTING	DATE:	7/19/2016
PROJECT:	ASRC WELL TEST UNIT 6 TRAILER	DRAWN BY:	M.A.
CUSTOMER:	TRIVAN	APPROVED BY:	M.A.
DESCRIPTION:	RIGGING DETAILS	SCALE:	AS SHOWN
		SHEET:	1 OF 1
